

[illegible]

ID	Task Name	Dura	Start	Finish	Predecessors	2022 February						2022 March																												2022 April						
						'22 Jan 31 01 02 03 04 05 06	'22 Feb 07 07 08 09 10 11 12	'22 Feb 14 13 14 15 16 17 18 19 20	'22 Feb 21 21 22 23 24 25 26 27	'22 Feb 28 28 01 02 03 04 05 06	'22 Mar 07 07 08 09 10 11 12 13	'22 Mar 14 14 15 16 17 18 19 20	'22 Mar 21 21 22 23 24 25 26 27	'22 Mar 28 28 29 30 31 01 02 03	'22 Apr 04 04 05 06 07																															
61	VSC defektacijos rezultatų patvirtinimas	3 days	Fri 23-02-17	Sun 23-02-19	60																																									
62	VSR 13 laipsnio darbo mentelių demontavimas	7 days	Mon 23-02-20	Sun 23-02-26	54																																									
63	VSR 13 laipsnio darbo mentelių pakeitimas	7 days	Mon 23-02-27	Sun 23-03-05	62																																									
64	VSR 13 laipsnio bandažų pratekinimas	3 days	Mon 23-03-06	Wed 23-03-08	63																																									
65	VSR balansavimas su Užsakovo turimomis švytuoklinėmis staklėmis	2 days	Thu 23-03-09	Fri 23-03-10	64																																									
66	VSC tūtinio aparato demontavimas	7 days	Mon 23-02-06	Sun 23-02-12	50																																									
67	VSC tūtinio aparato pakeitimas nauju	7 days	Mon 23-02-13	Sun 23-02-19	66																																									
68	VSC diafragmų ir apkabų percentravimas, šiluminių tarpų	7 days	Thu 23-03-30	Wed 23-04-05	26;56;57;58;67																																									
69	VSC diafragminių sandarinimų tarpų priderinimas, šiluminių tarpų	6 days	Thu 23-04-06	Tue 23-04-11	58;68																																									
70	VSC galinių ir tepalinių sandarinimų tarpų priderinimas, šiluminių tarpų	6 days	Wed 23-04-12	Mon 23-04-17	69;65																																									
71	VSC pratėkamos dalies tarpų kontrolinis patikrinimas. VSC paruošimas	4 days	Tue 23-04-18	Fri 23-04-21	70																																									
72	VSC išorinio korpuso surinkimas ir uždarymas. VSR garinio išbėgio patikrinimas. VSC smeigių karštas užveržimas	5 days	Sat 23-04-22	Wed 23-04-26	59;71																																									
73	Generatoriaus remontas																																													
74	20 kV šynlaidžių atjungimas nuo generatoriaus (vykdo Užsakovas)	1 day	Mon 23-01-09	Mon 23-01-09																																										
75	Alyvos vamzdynų atjungimas, GSS išardymas	2 days	Tue 23-01-10	Wed 23-01-11	74																																									
76	Generatoriaus virštutinių ir apatinių dangčių nuėmimas, difuzorių ir tepalo gaudyklių tarpų matavimas	8 days	Thu 23-01-12	Thu 23-01-19	75																																									
77	Tepalo gaudyklių nuėmimas	4 days	Fri 23-01-20	Mon 23-01-23	76																																									
78	Oro tarpų tarp rotorius ir statorius geležies matavimai pagal formuliarą	2 days	Tue 23-01-24	Wed 23-01-25	77																																									
79	Alyvos vamzdynų atjungimas, 7-to guolio kėdės demontavimas	2 days	Thu 23-01-26	Fri 23-01-27	78																																									
80	Generatoriaus rotoriaus ventiliatorių mentelių nuėmimas, paruošimas defektoskopijai.	7 days	Sat 23-01-28	Fri 23-02-03	79																																									
81	Generatoriaus rotoriaus ištraukimas iš statorius	6 days	Sat 23-02-04	Thu 23-02-09	80																																									
82	Generatoriaus rotoriaus ventiliatorių mentelių defektoskopijos, pagal aplinkraščio Nr. E-1/81 (TS Priedo Nr. 1 dokumentas Nr. 18) reikalavimus, atlikimas. Įtrūkimų šalinimas.	7 days	Fri 23-02-10	Thu 23-02-16	81																																									
83	Gen. Veleno kakliukų ir guolių paviršių šiurkštumo ir ovališko patikrinimas	1 day	Tue 23-02-14	Tue 23-02-14	81																																									
Project: T-8 remonto grafikas 2 Date: Tue 22-09-27		Task	<div></div>	Inactive Task	<div></div>	Manual Summary Rollup	<div></div>	External Milestone	<div></div>	Manual Progress																																				
		Split	<div></div>	Inactive Milestone	<div></div>	Manual Summary	<div></div>	Deadline	<div></div>																																					
		Milestone	<div></div>	Inactive Summary	<div></div>	Start-only	<div></div>	Critical	<div></div>																																					
		Summary	<div></div>	Manual Task	<div></div>	Finish-only	<div></div>	Critical Split	<div></div>																																					
		Project Summary	<div></div>	Duration-only	<div></div>	External Tasks	<div></div>	Progress	<div></div>																																					
Page 4																																														


[illegible]


																															2022 August							2022 September														2022 October														2022 November																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
'22 Jul 25							'22 Aug 01							'22 Aug 08							'22 Aug 15							'22 Aug 22							'22 Aug 29							'22 Sep 05							'22 Sep 12							'22 Sep 19							'22 Sep 26							'22 Oct 03							'22 Oct 10							'22 Oct 17							'22 Oct 24							'22 Oct 31							'22 Nov 07																																																																																																																																																																																																																																																																																																																																																																																																																																																					
25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	0

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

The legend defines the symbols used in the Gantt chart:

- Task:** Solid blue bar
- Inactive Task:** Dashed blue bar
- Manual Summary Rollup:** Solid teal bar
- External Milestone:** Diamond symbol
- Manual Progress:** Solid teal bar with a vertical line
- Split:** Dotted blue bar
- Inactive Milestone:** Diamond symbol
- Manual Summary:** Solid black bar
- Deadline:** Green downward arrow
- Milestone:** Diamond symbol
- Inactive Summary:** Dashed grey bar
- Start-only:** Teal bar with a left bracket
- Critical:** Solid red bar
- Summary:** Solid black bar with a right bracket
- Manual Task:** Solid teal bar with a right bracket
- Finish-only:** Teal bar with a left bracket
- Critical Split:** Dotted red bar
- Project Summary:** Dashed grey bar with a right bracket
- Duration-only:** Solid teal bar with a right bracket
- External Tasks:** Solid grey bar
- Progress:** Solid blue bar

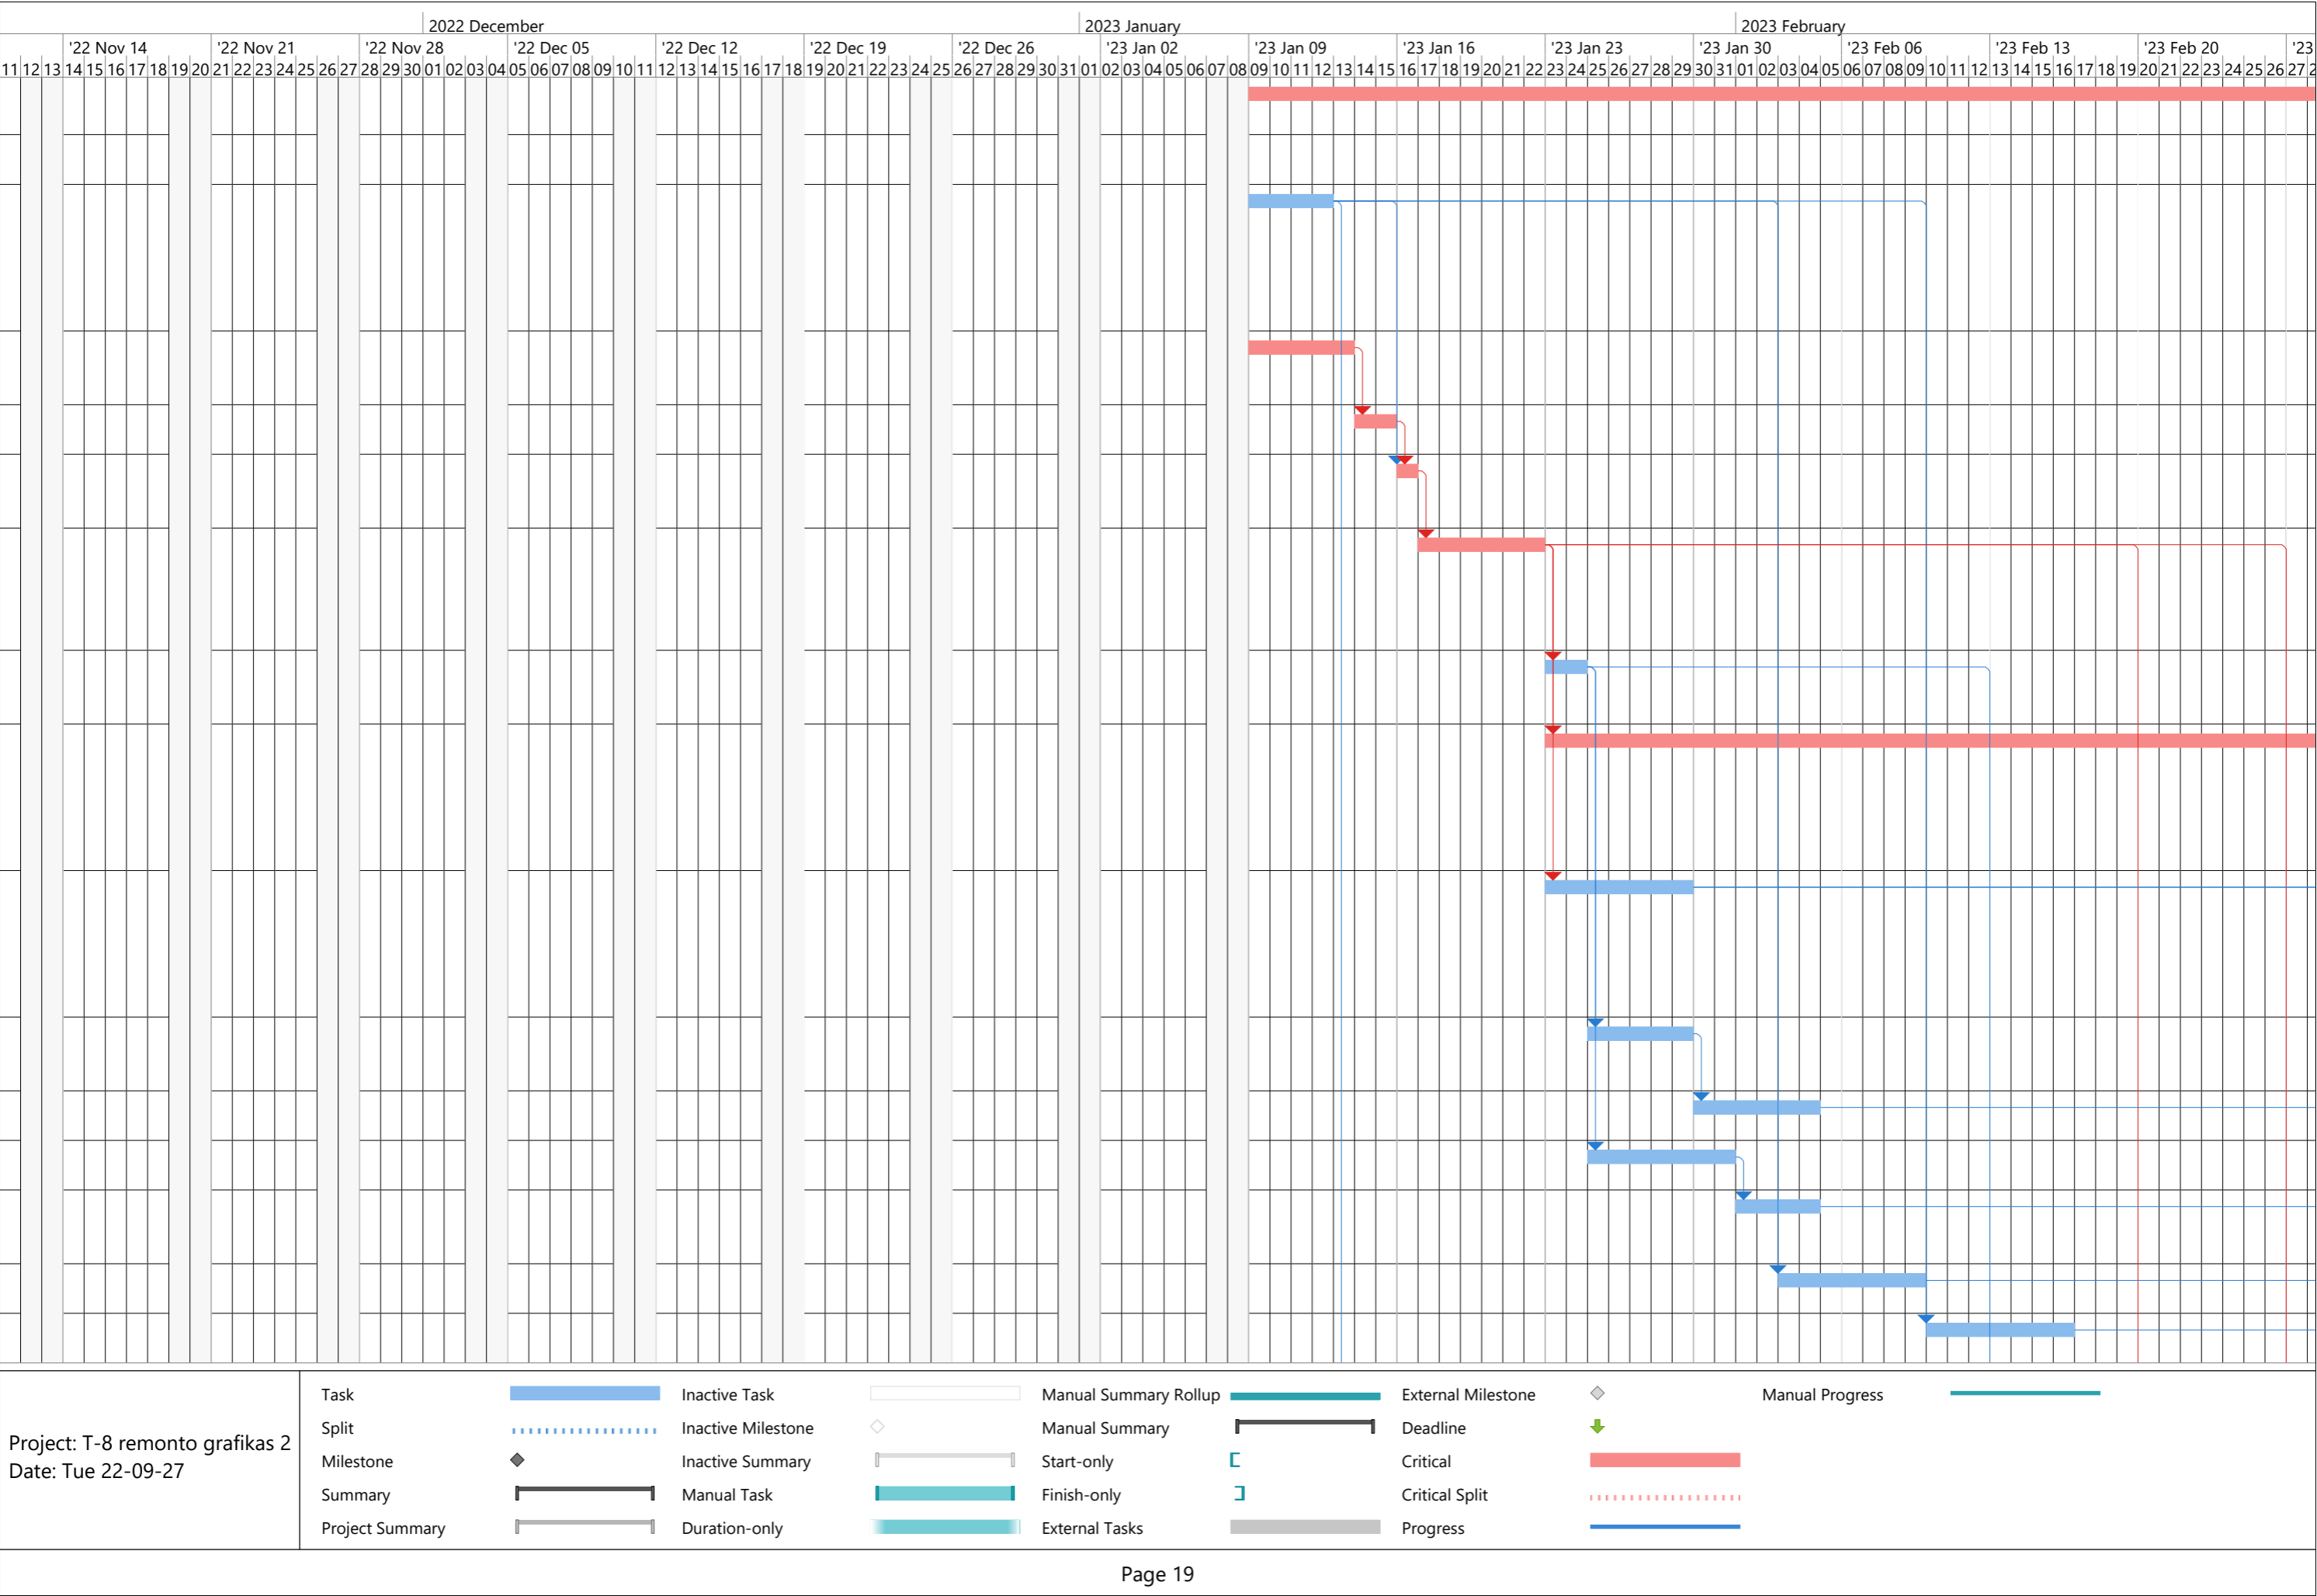

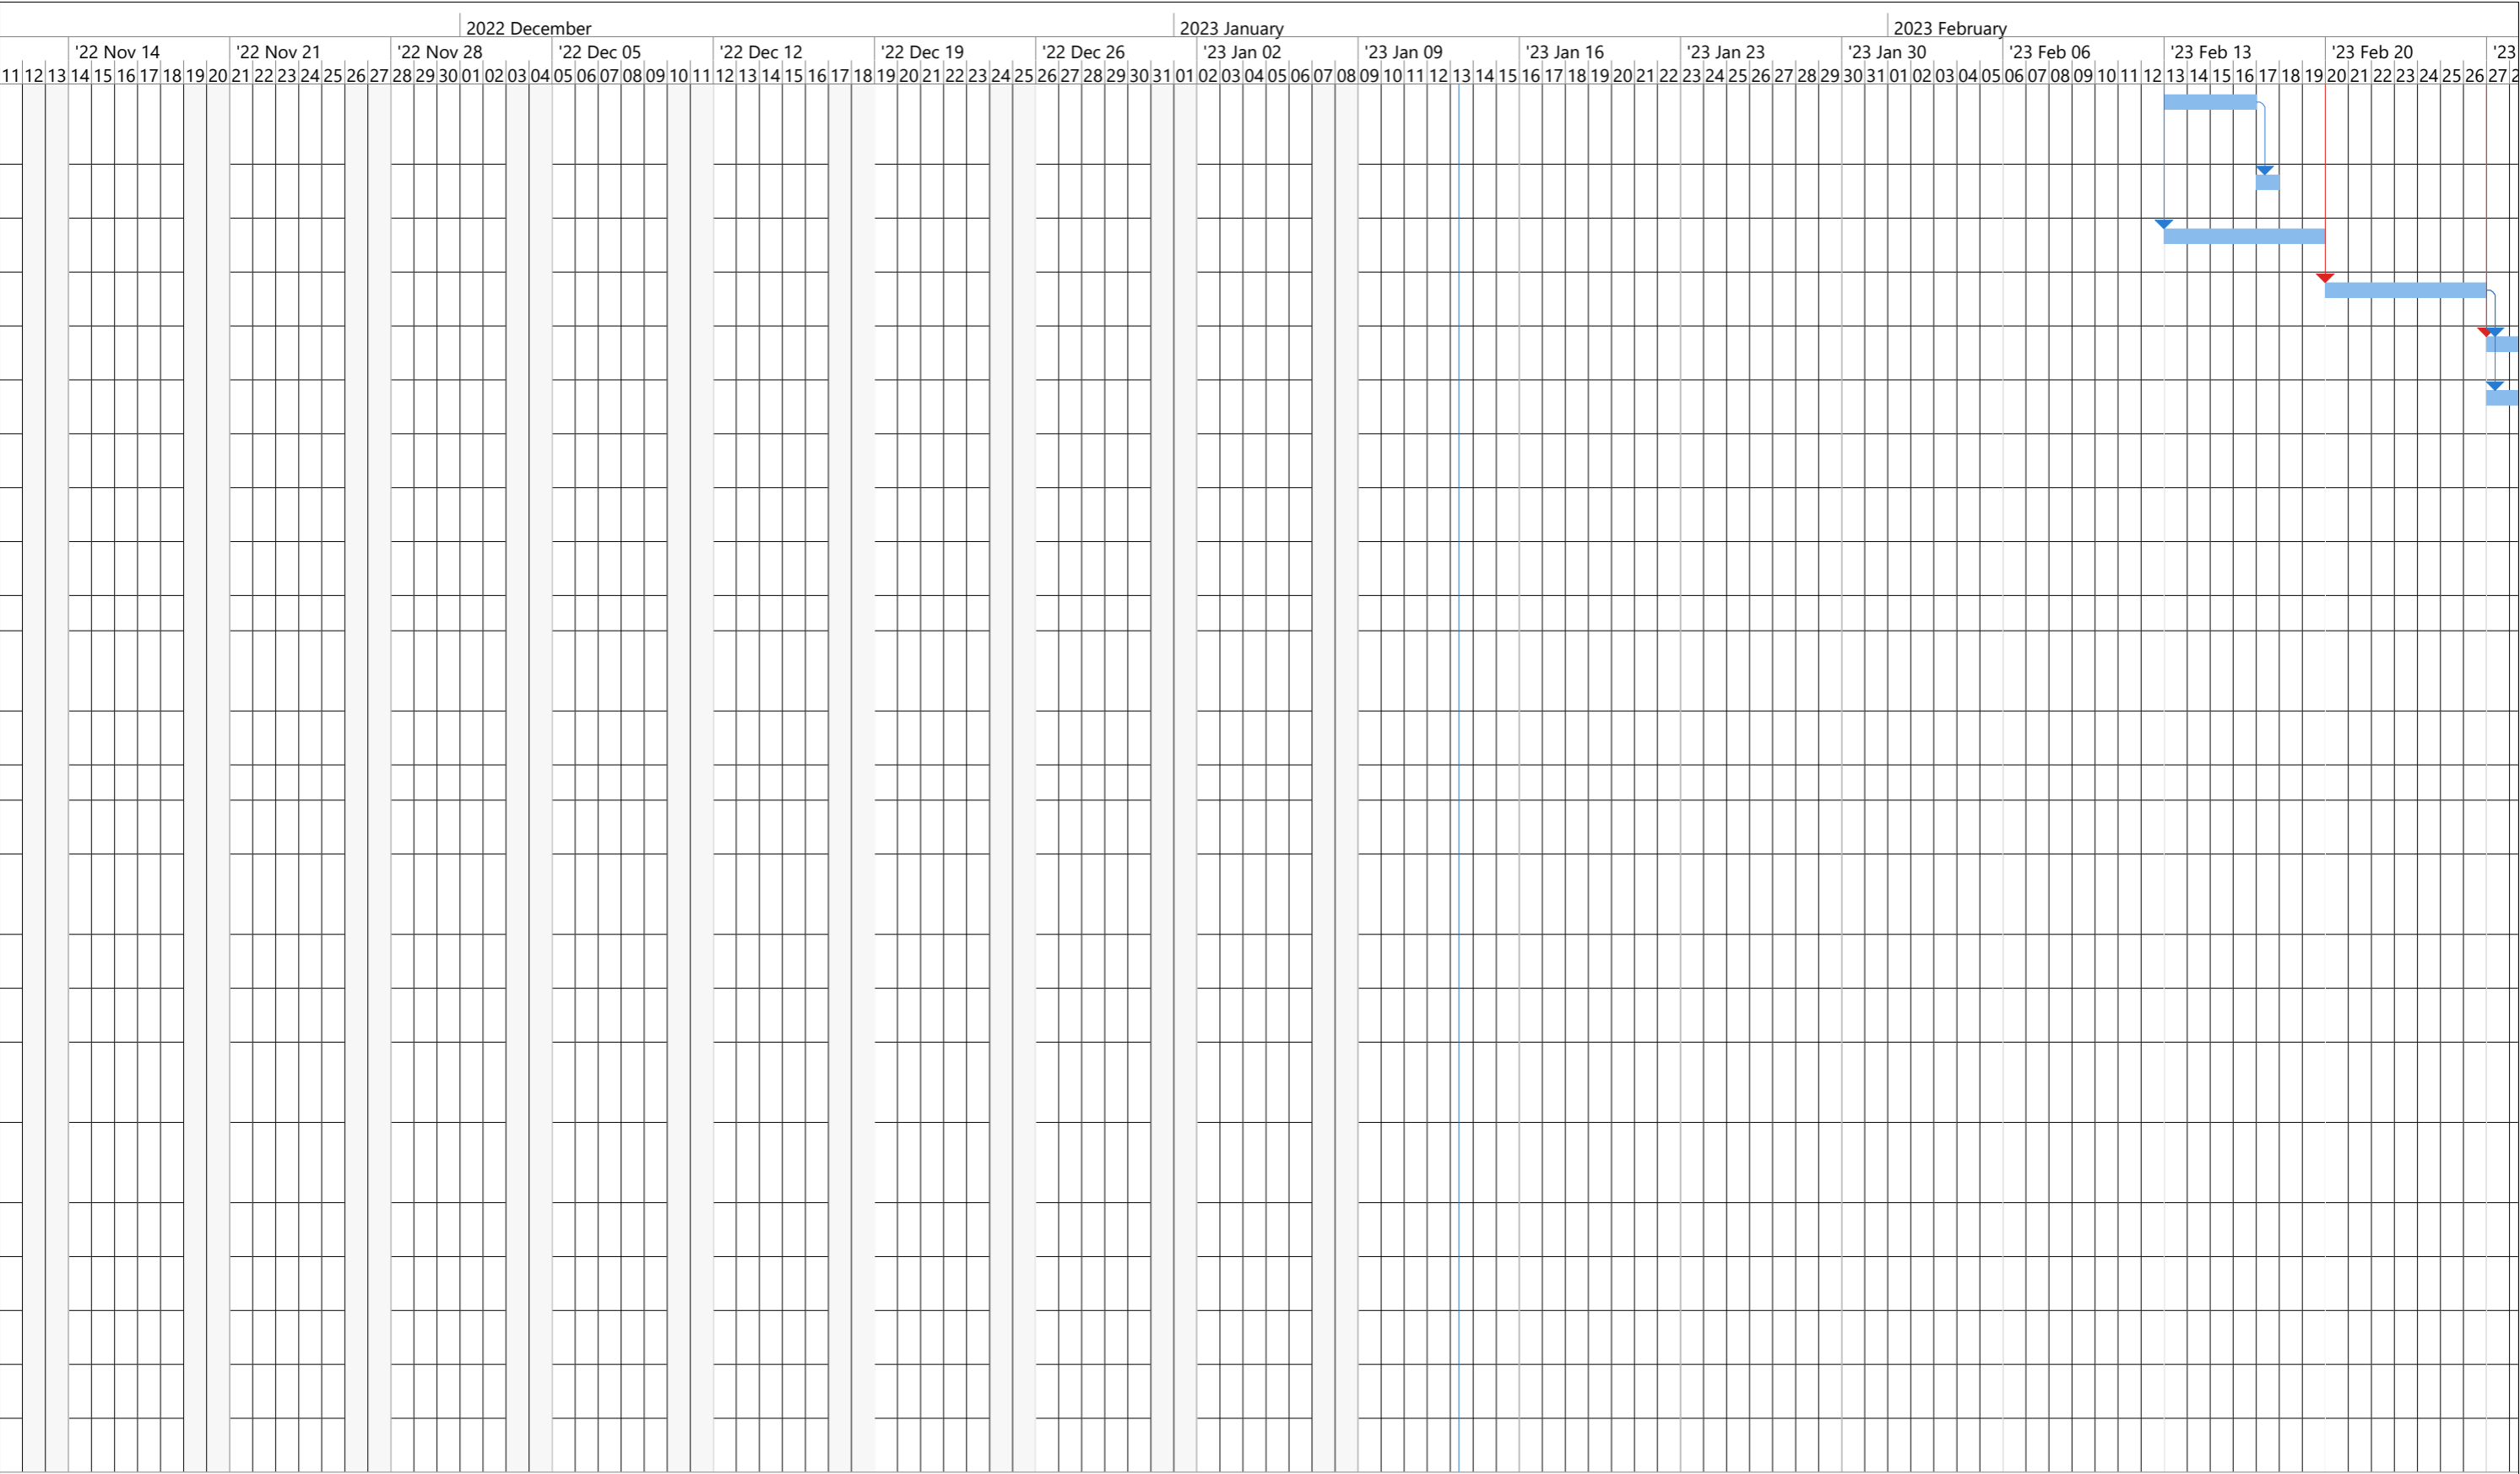

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline


Critical

Critical Split

Progress

Manual Progress

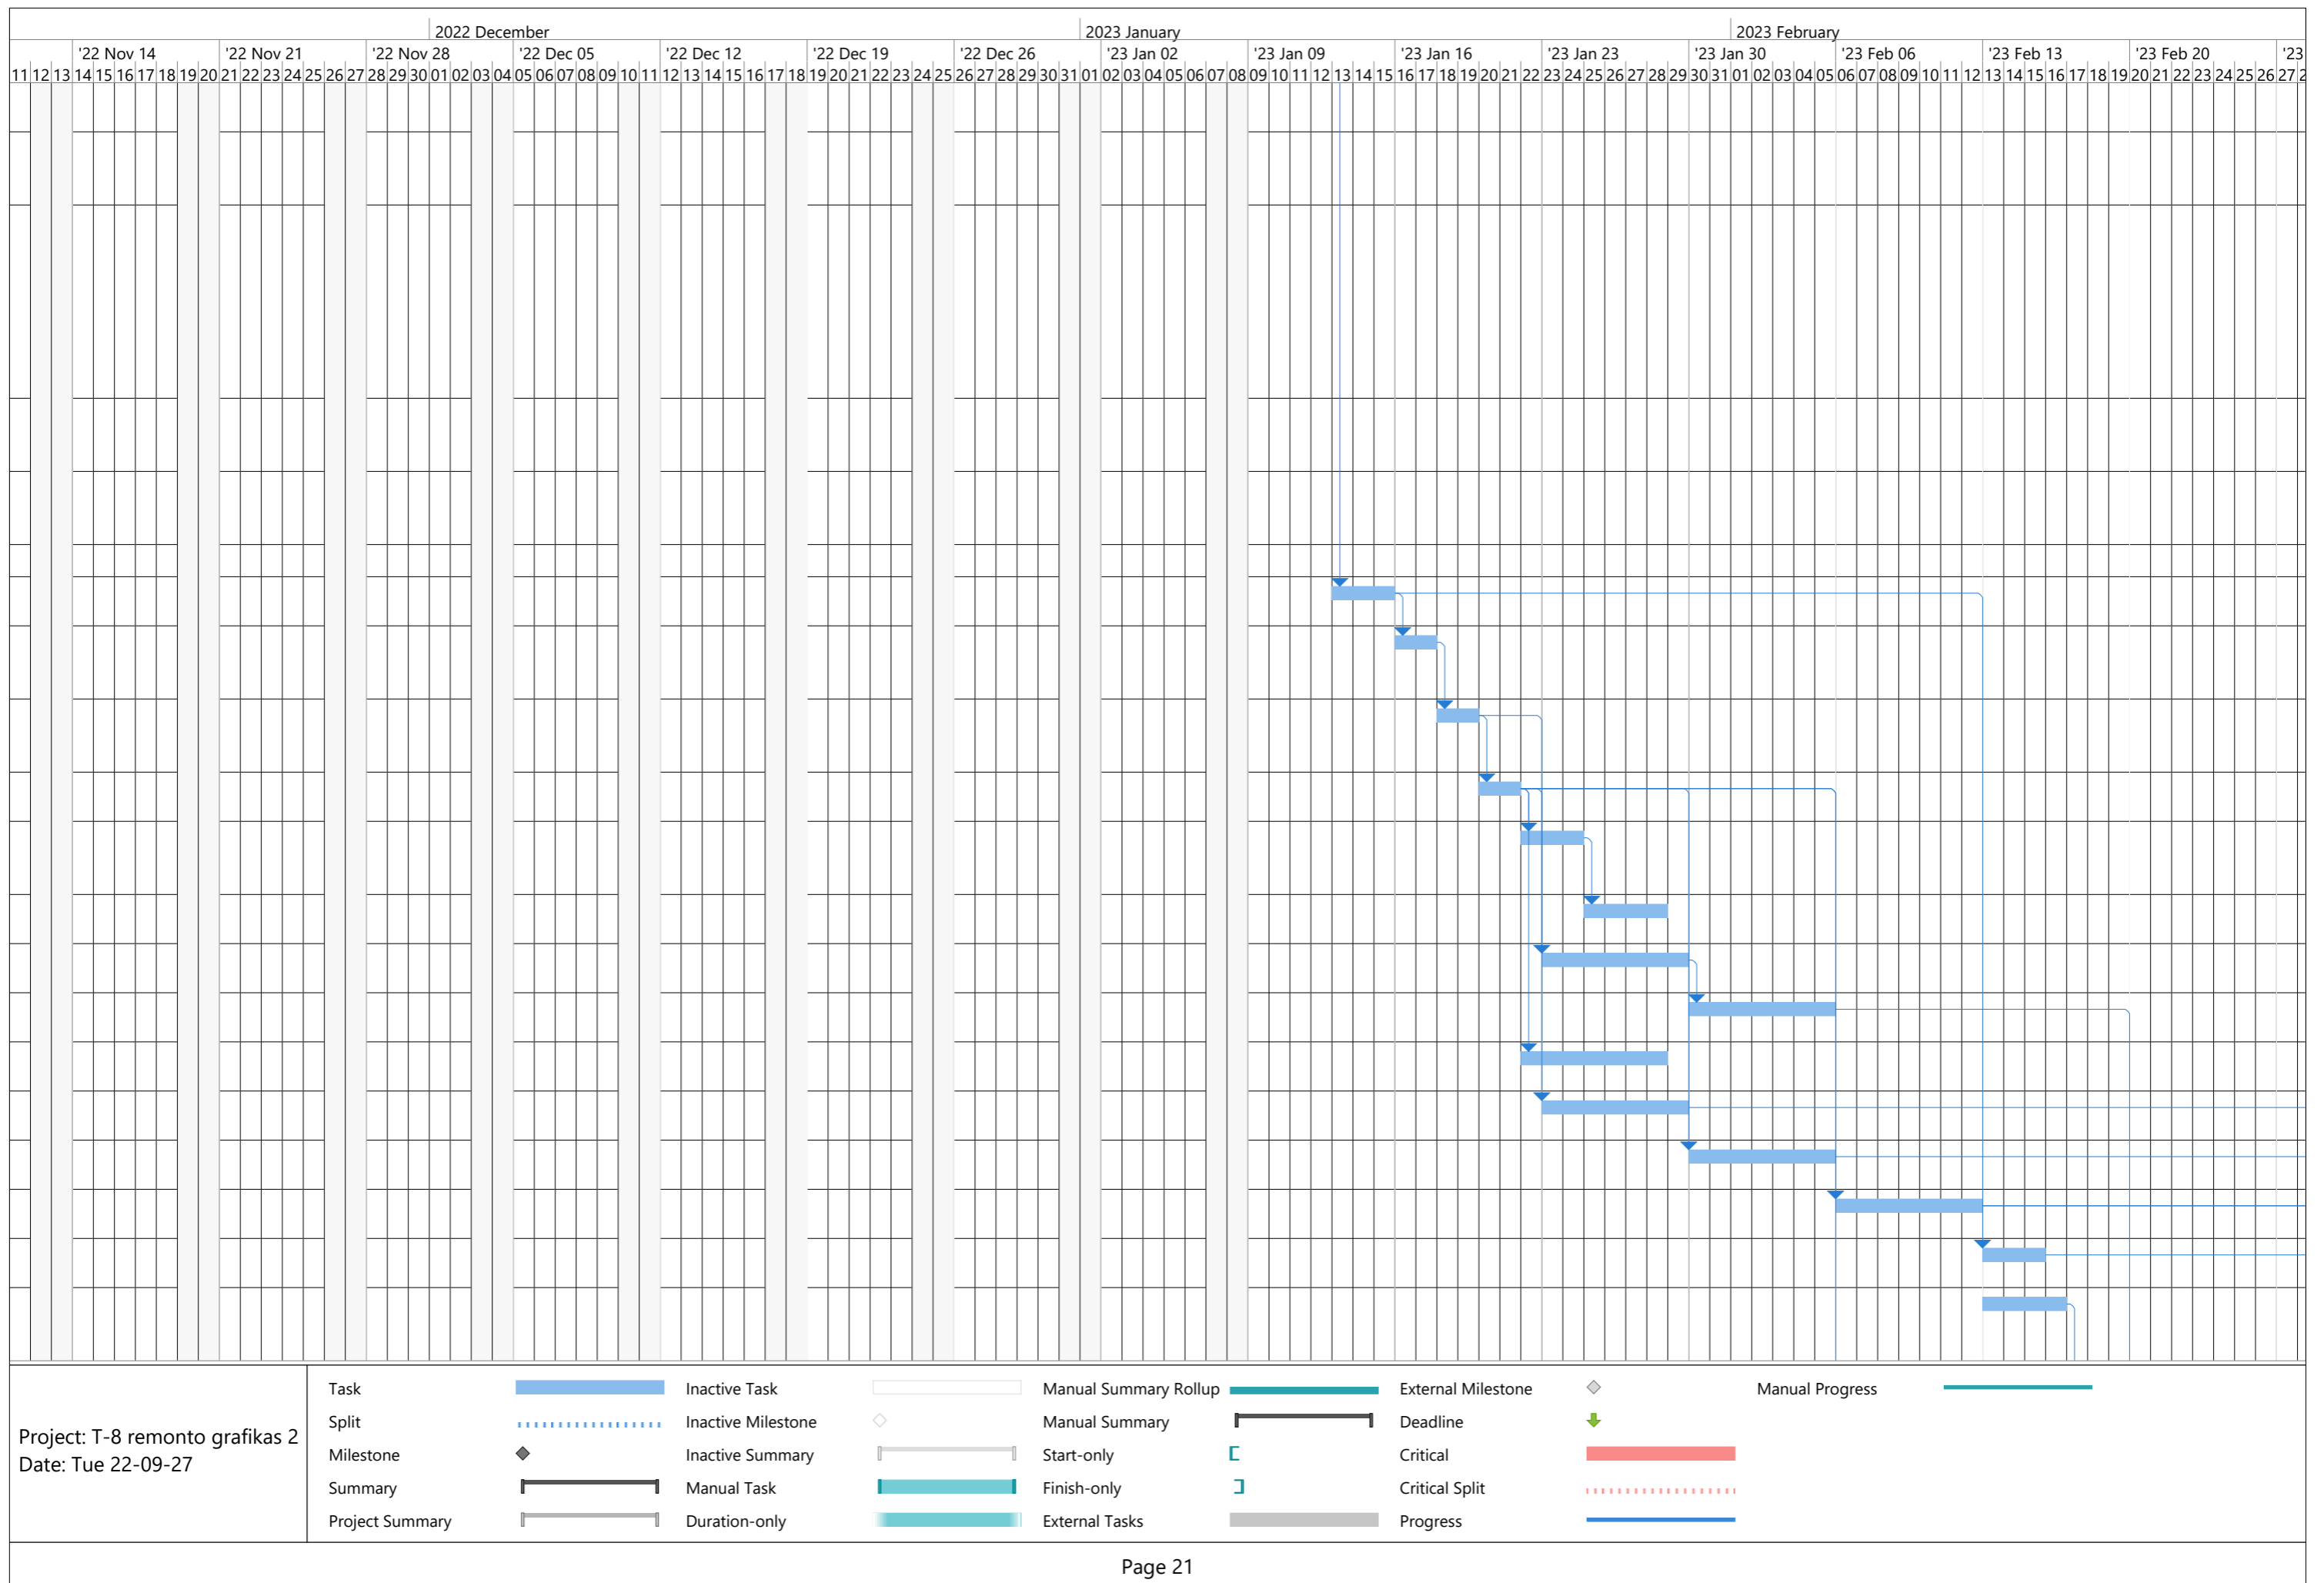

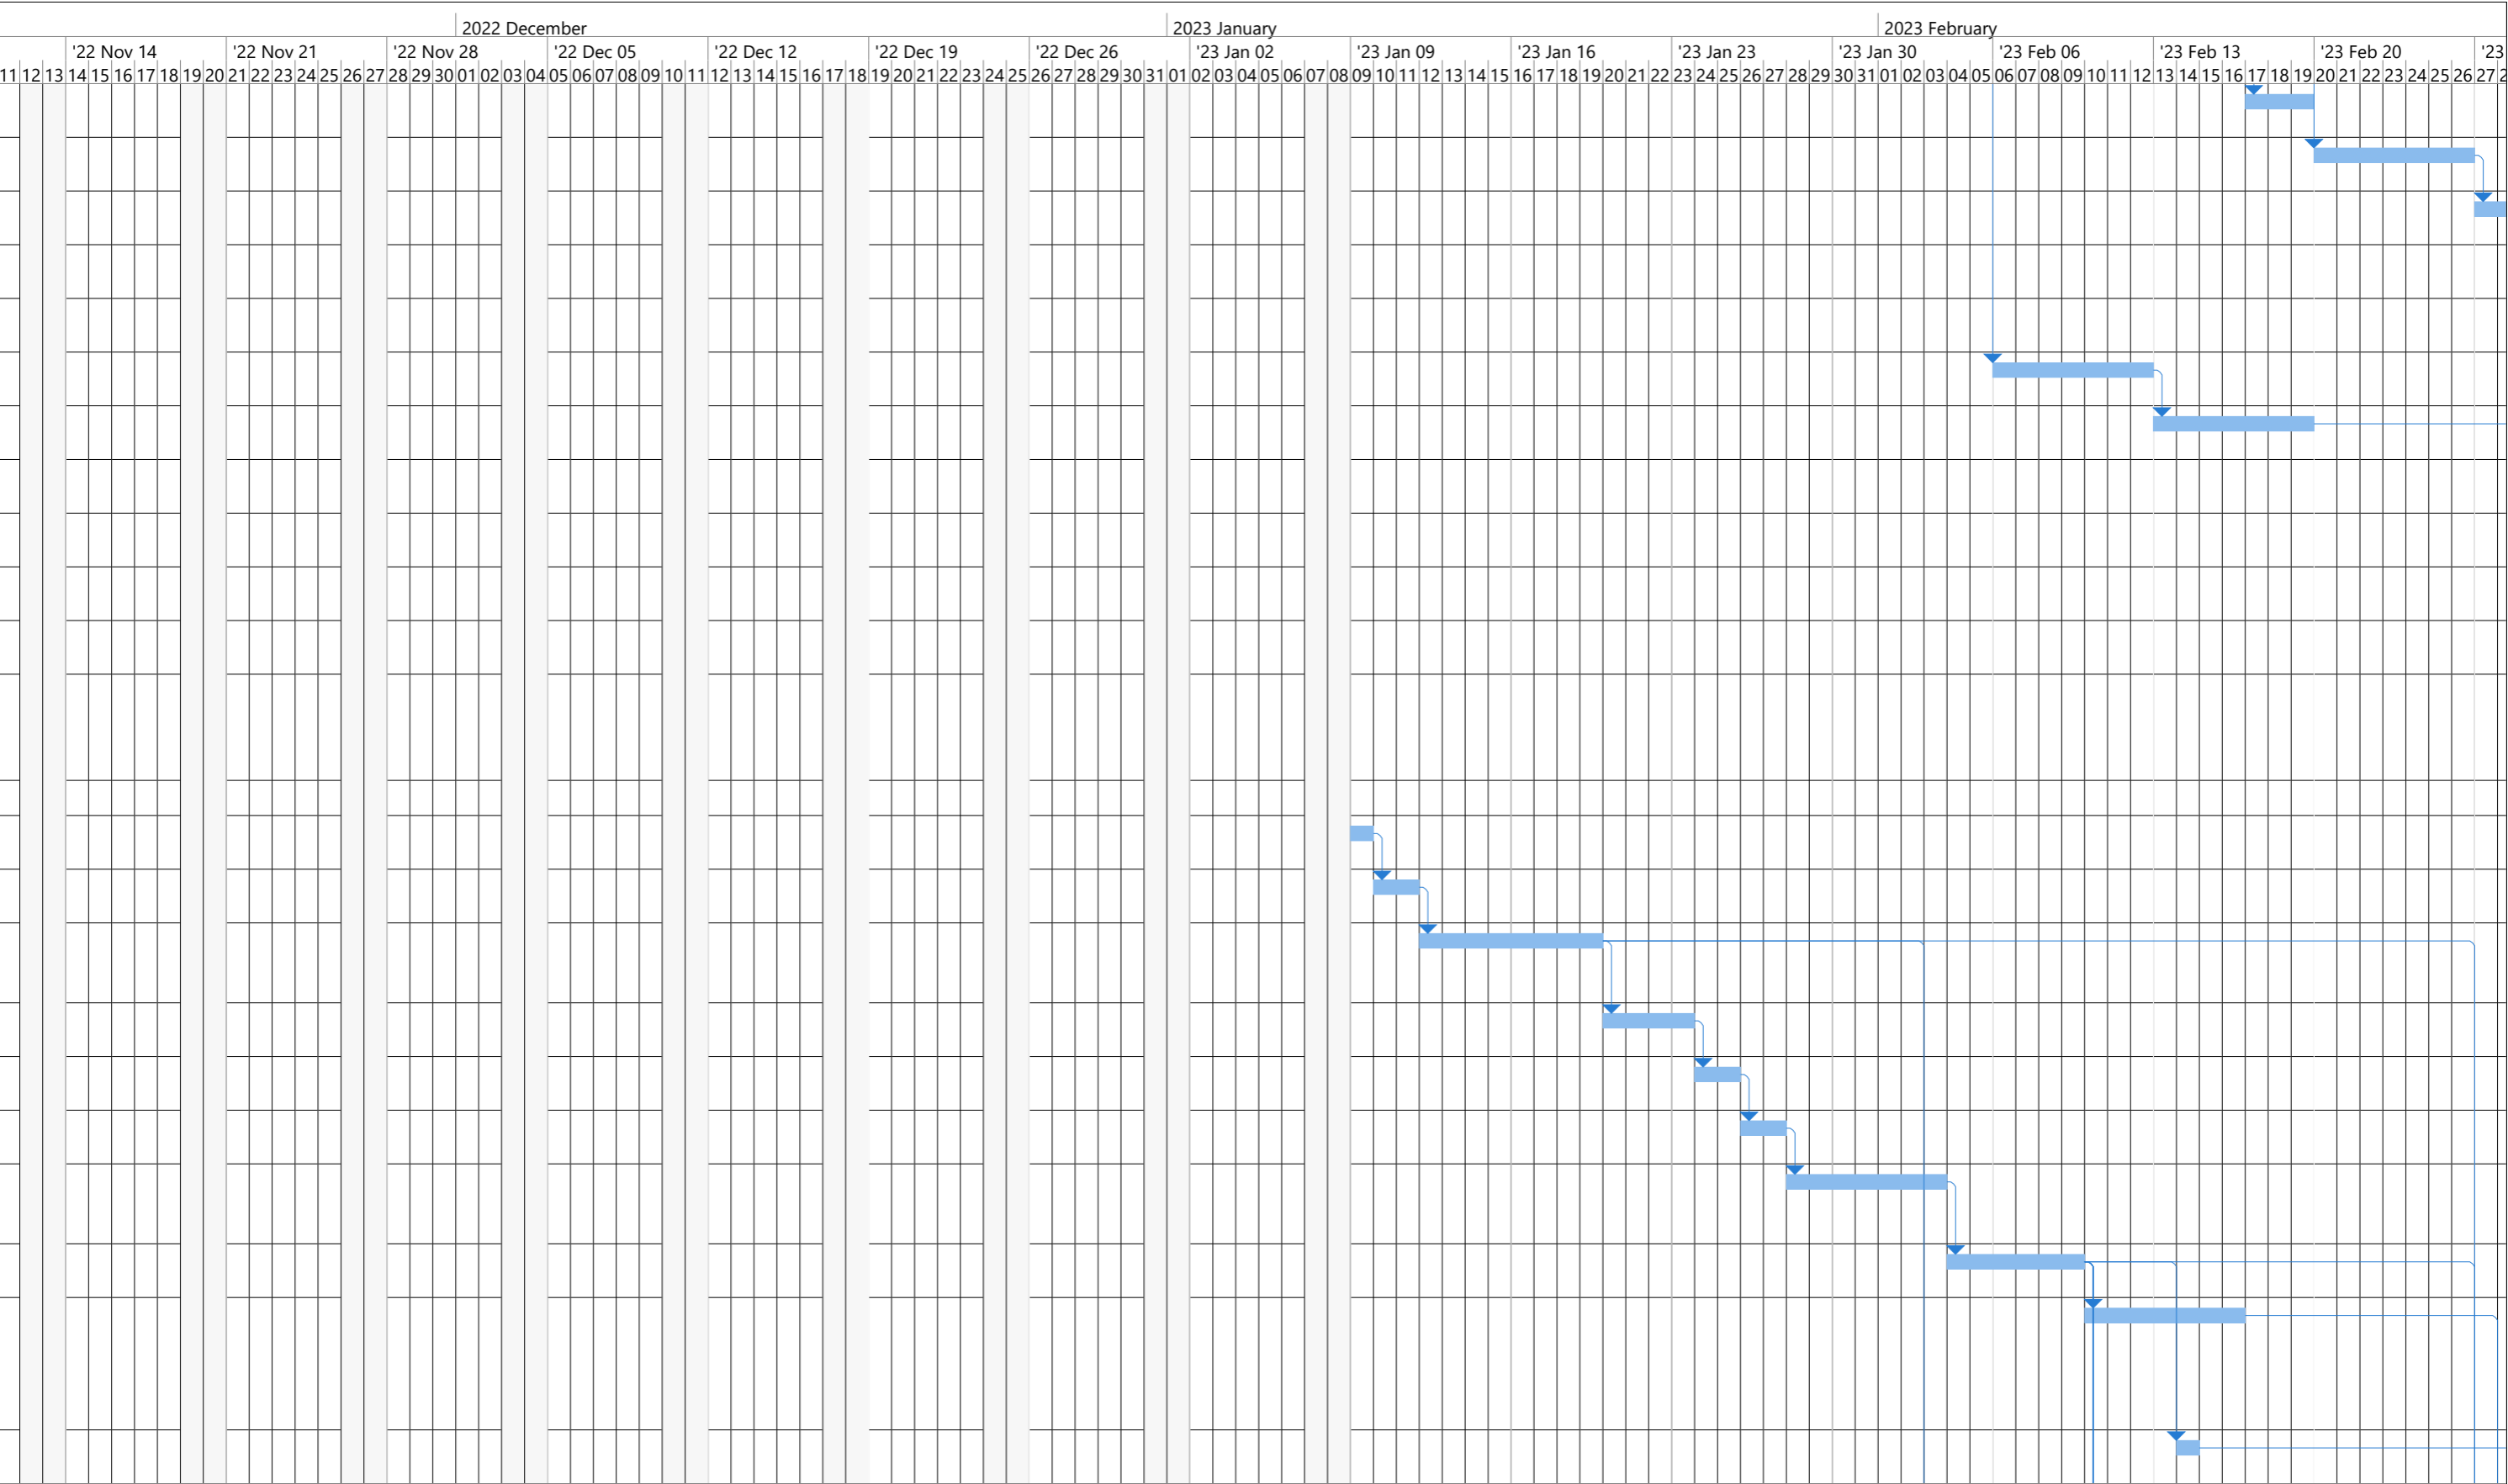

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress



Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Critical

Critical Split

Progress

Manual Progress

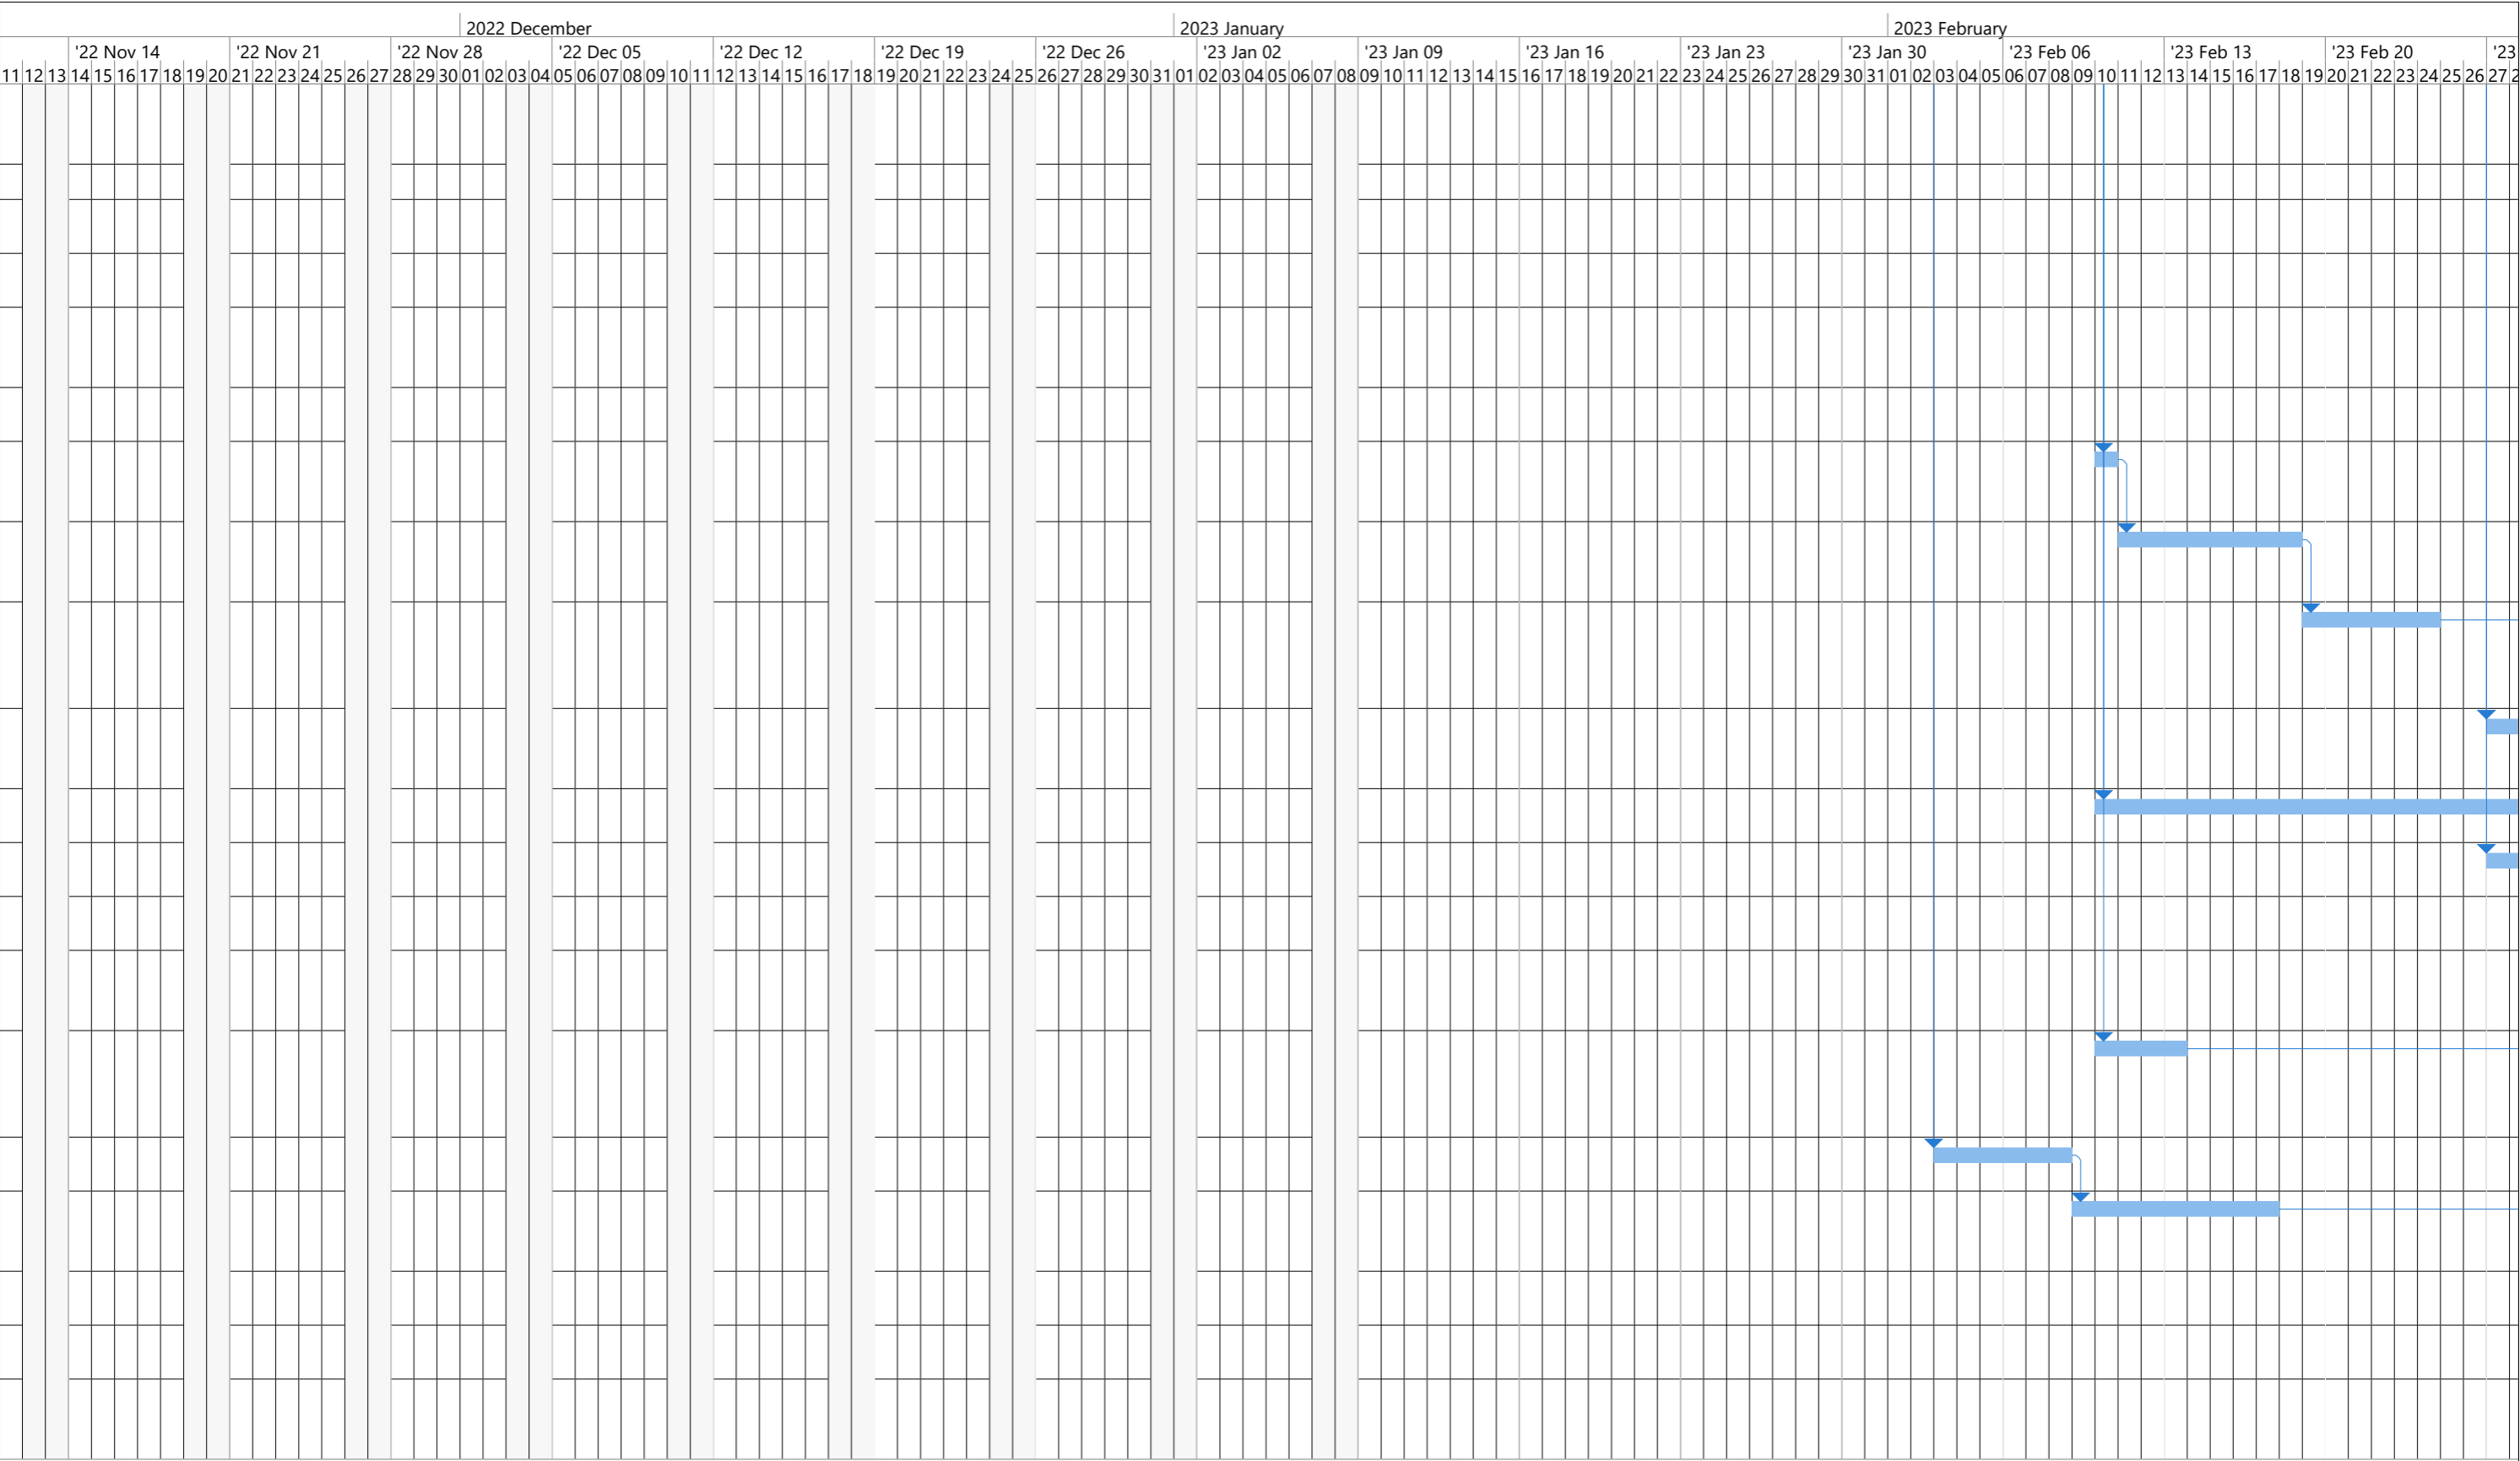

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Critical

Critical Split

Progress

Manual Progress

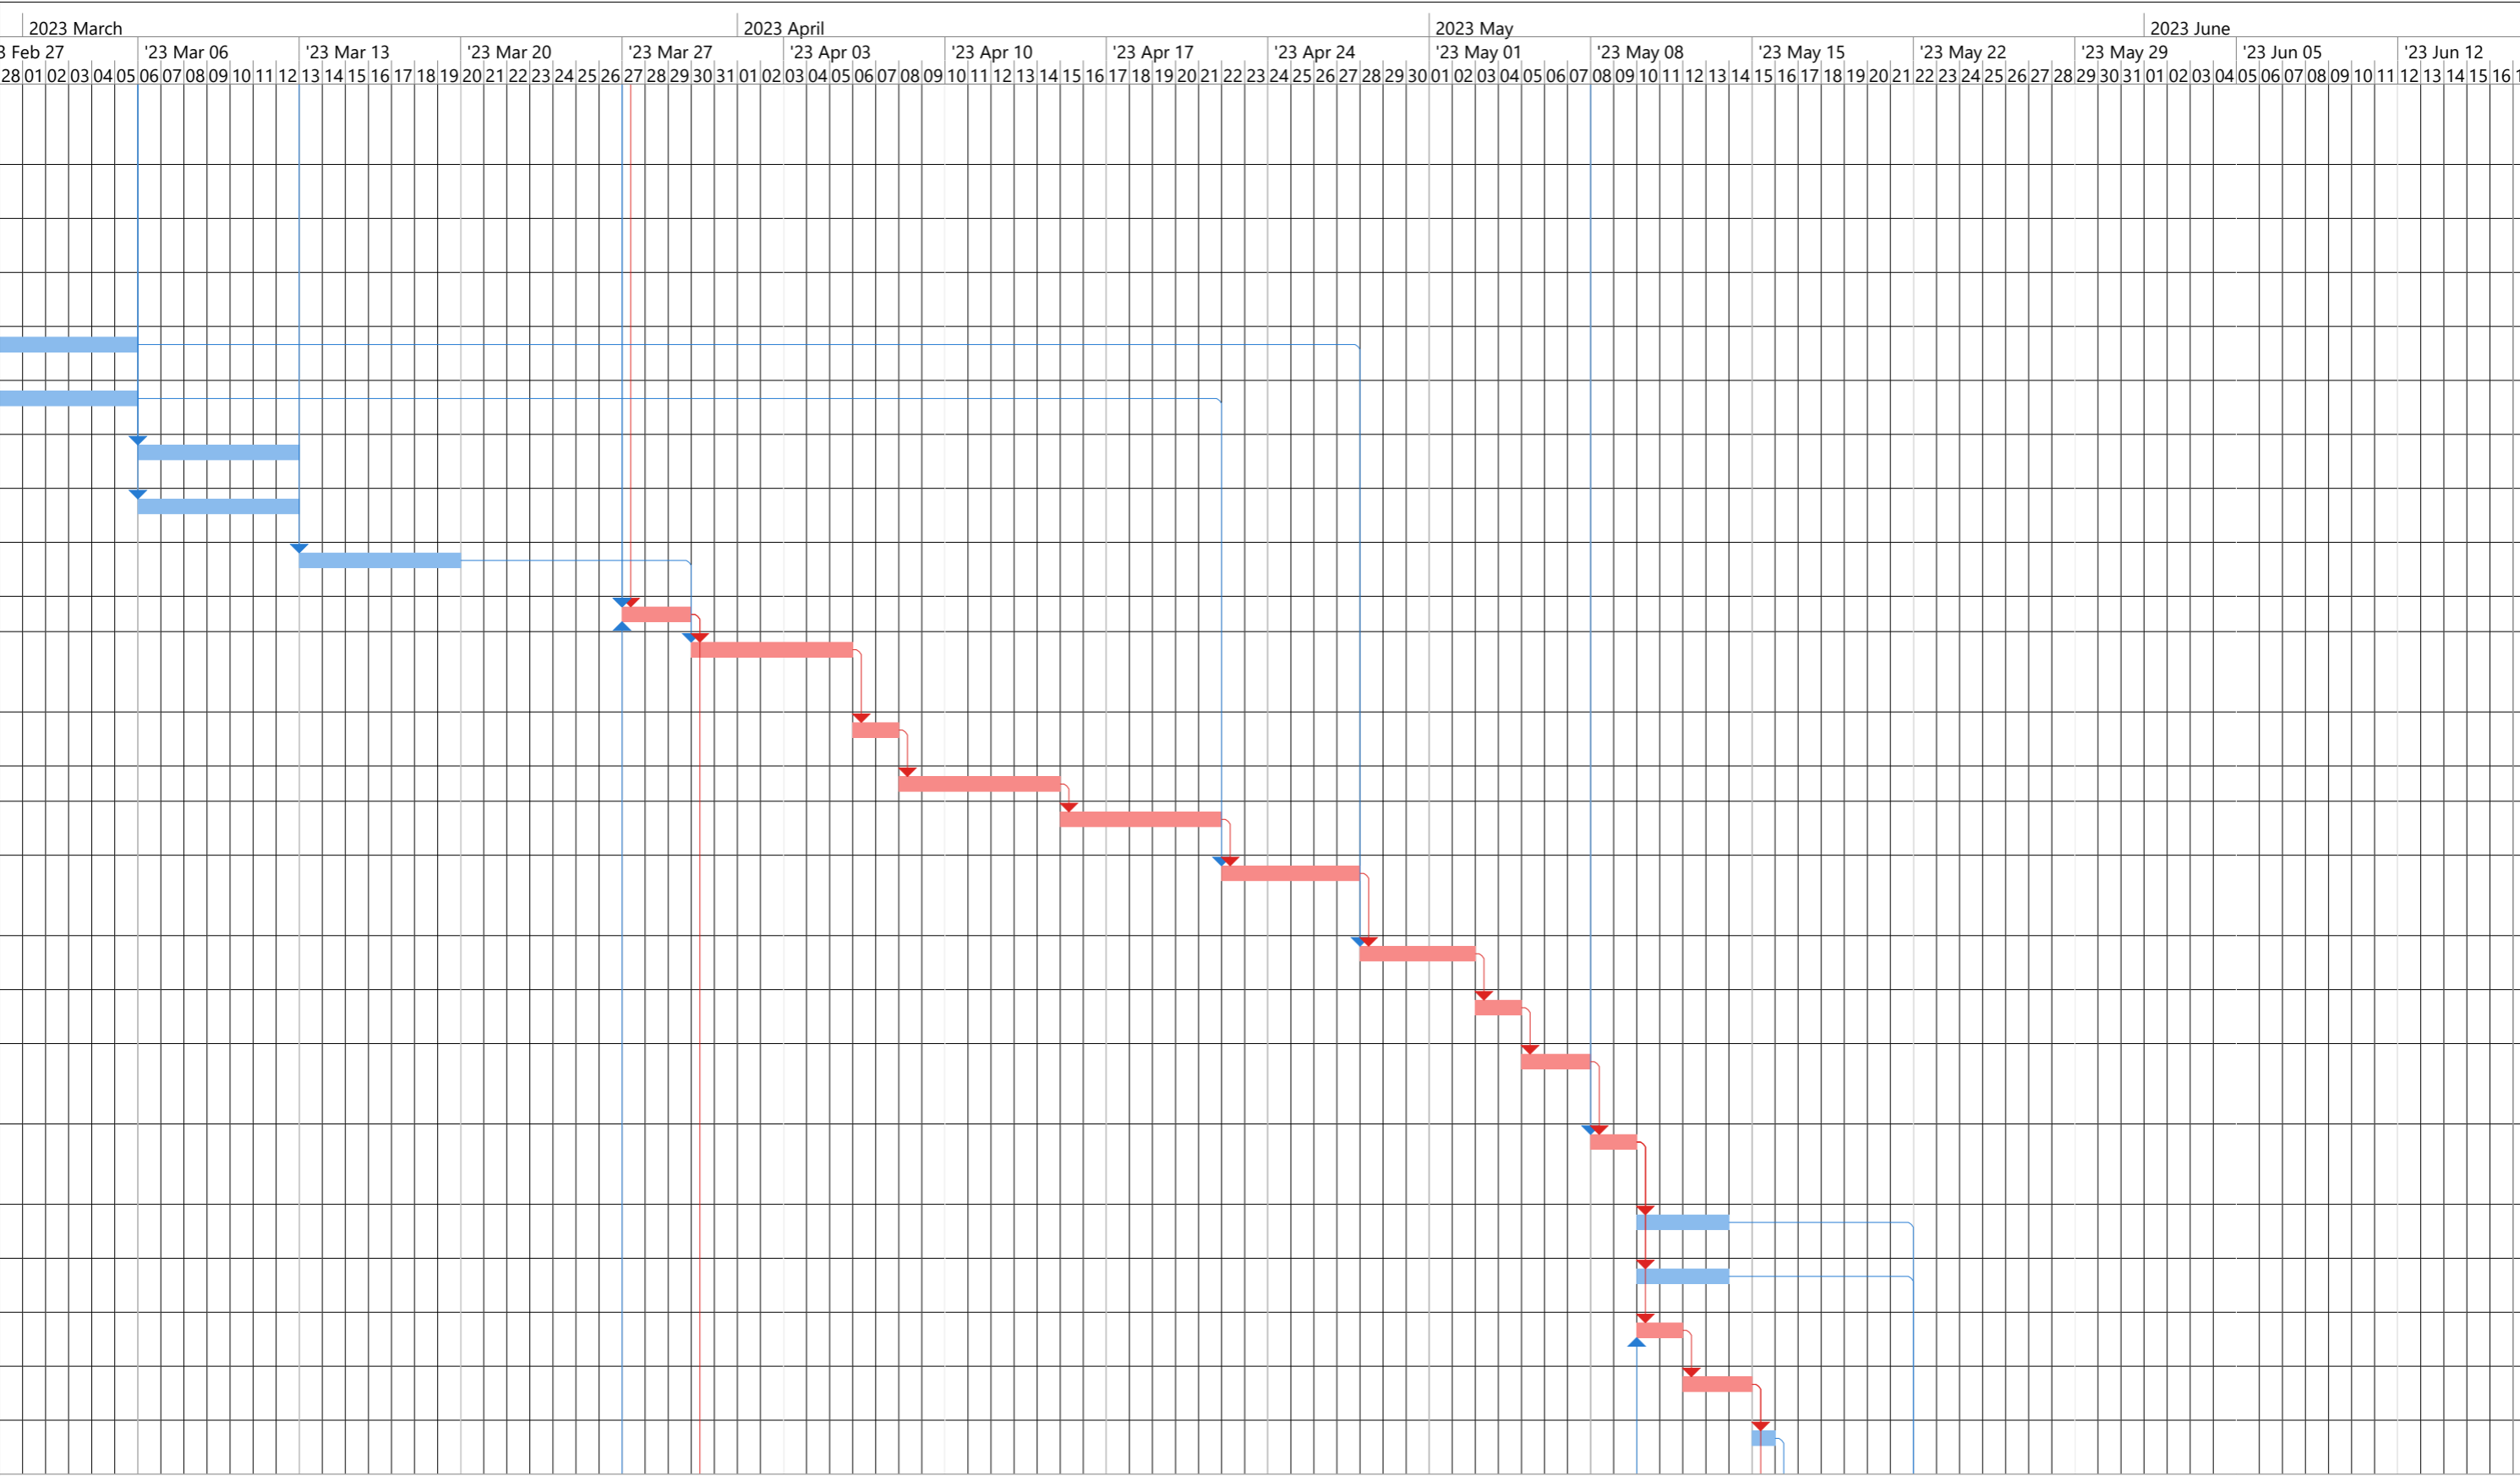

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27


Task

Split

Milestone

Summary

Project Summary



Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only



Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks





External Milestone

Deadline

Critical


Critical Split

Progress



Manual Progress



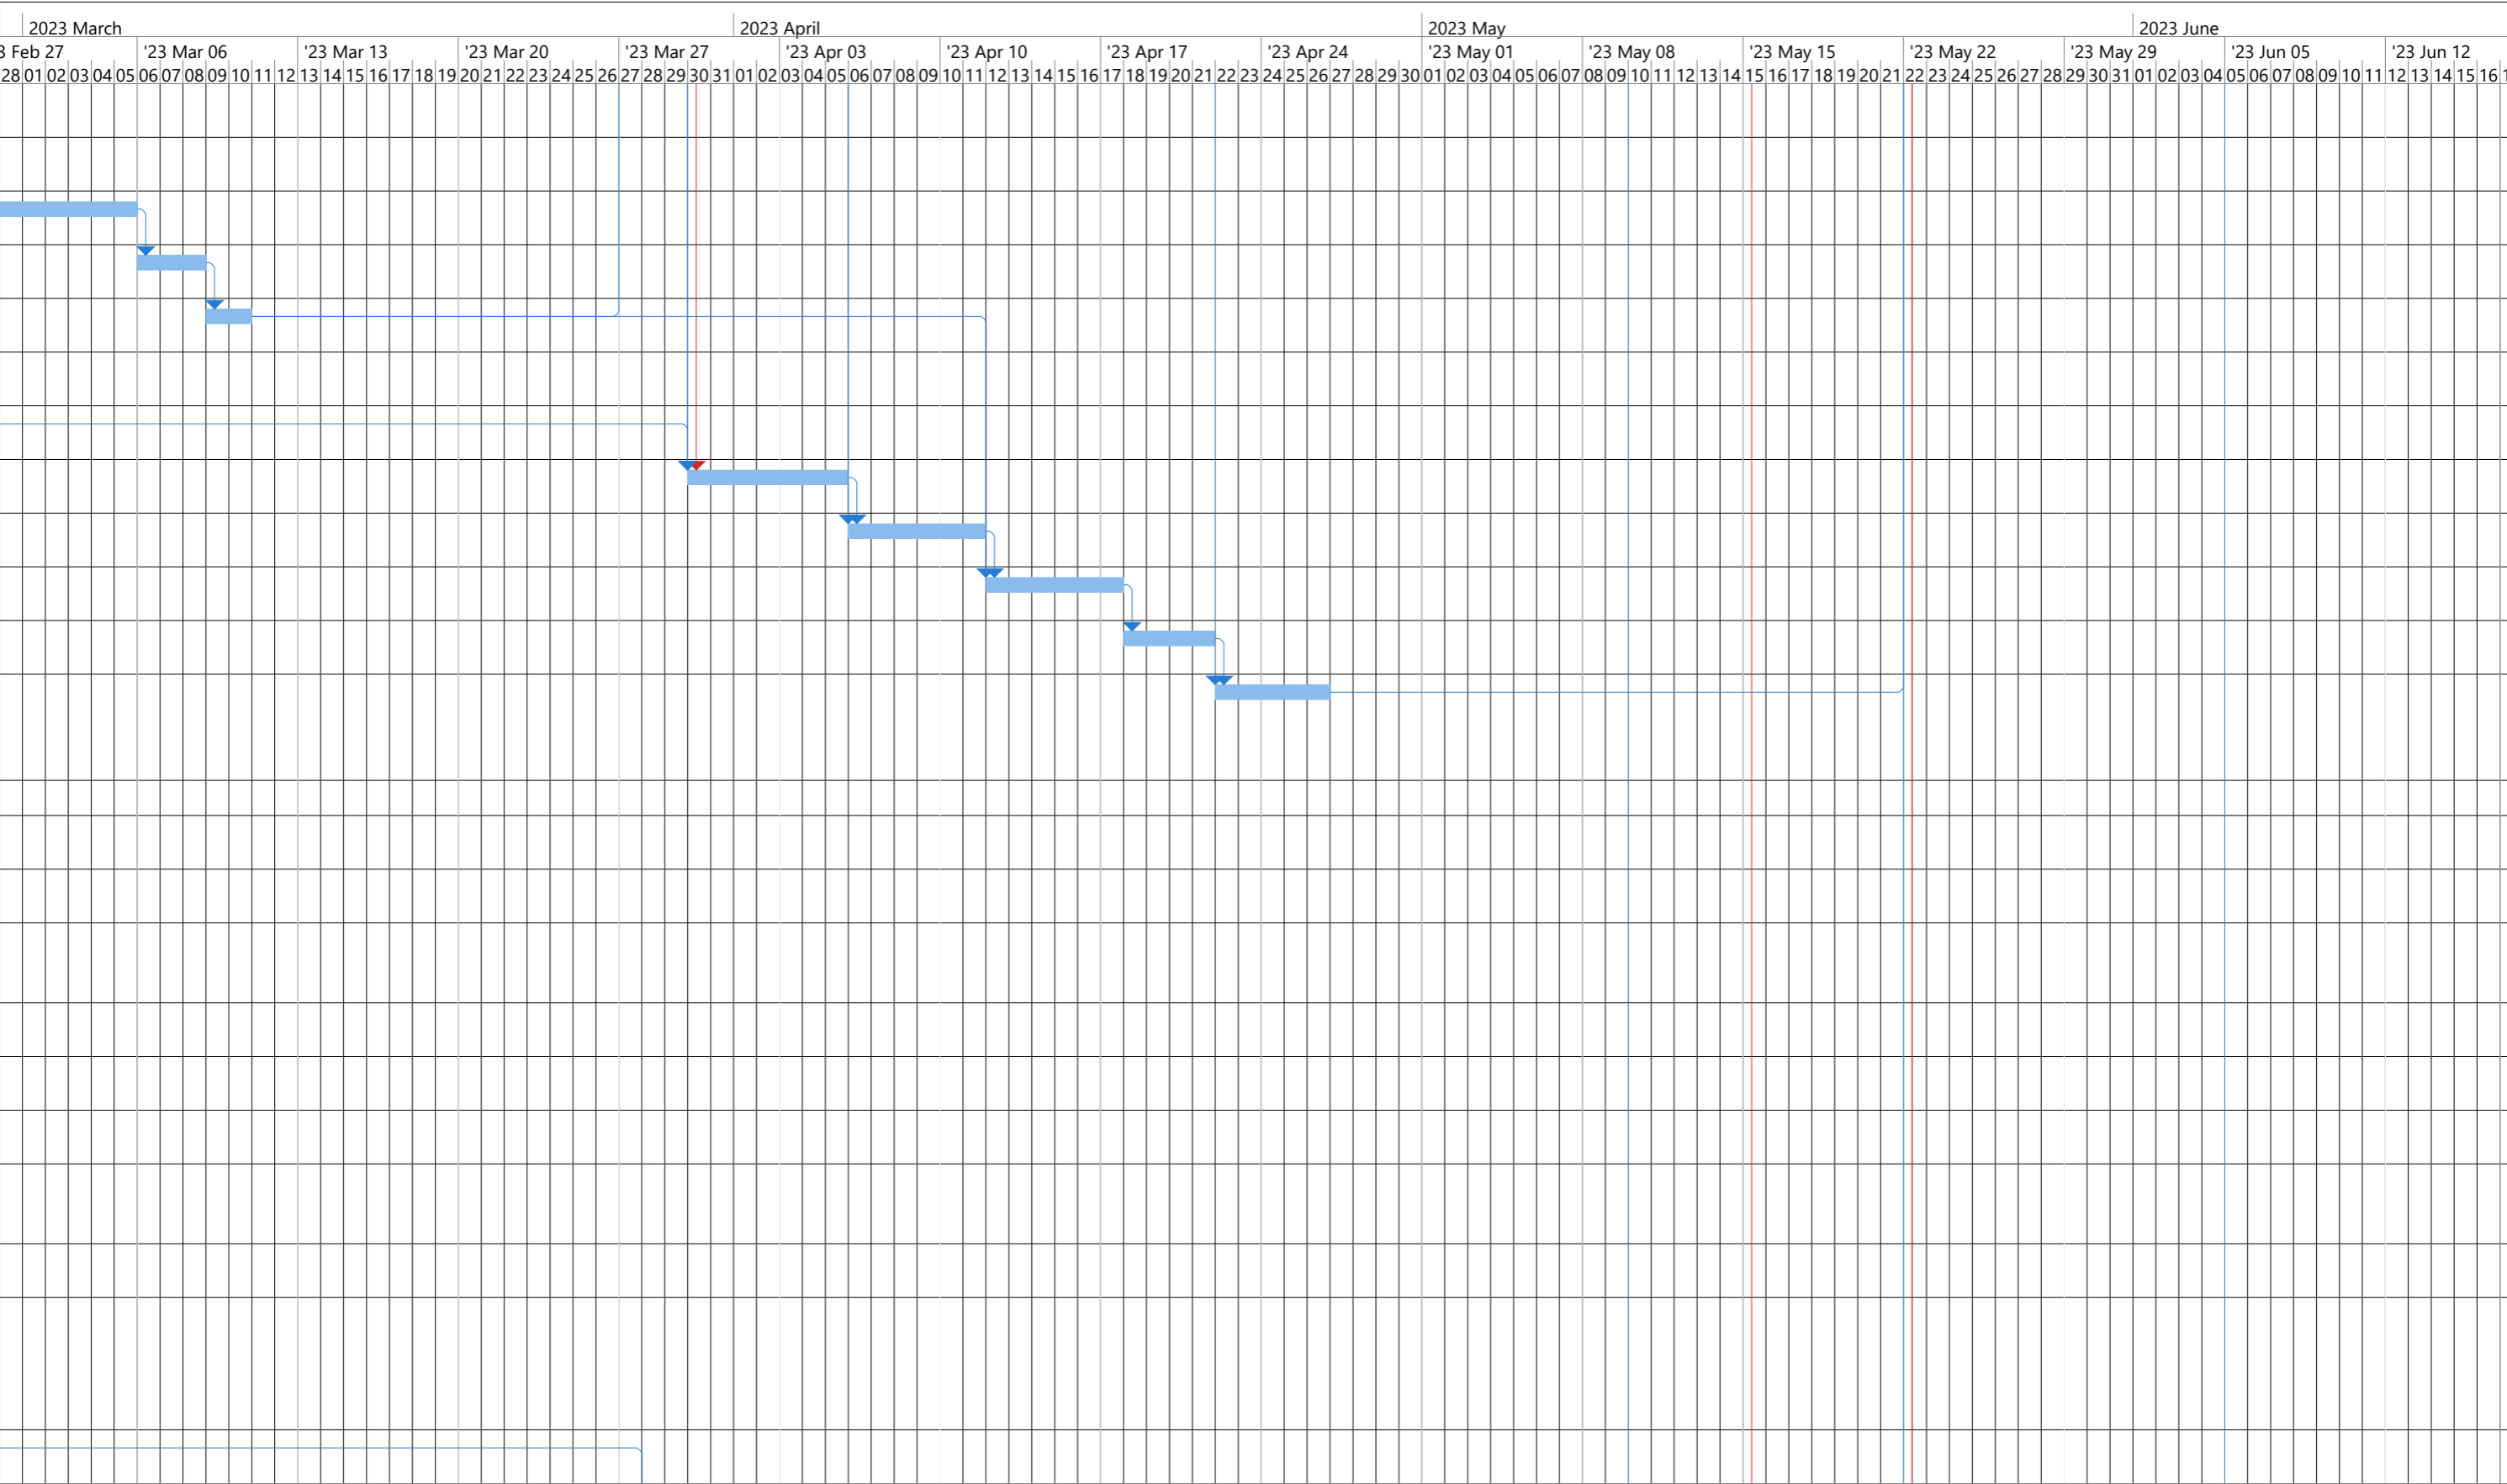

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Critical

Critical Split


Progress

Manual Progress

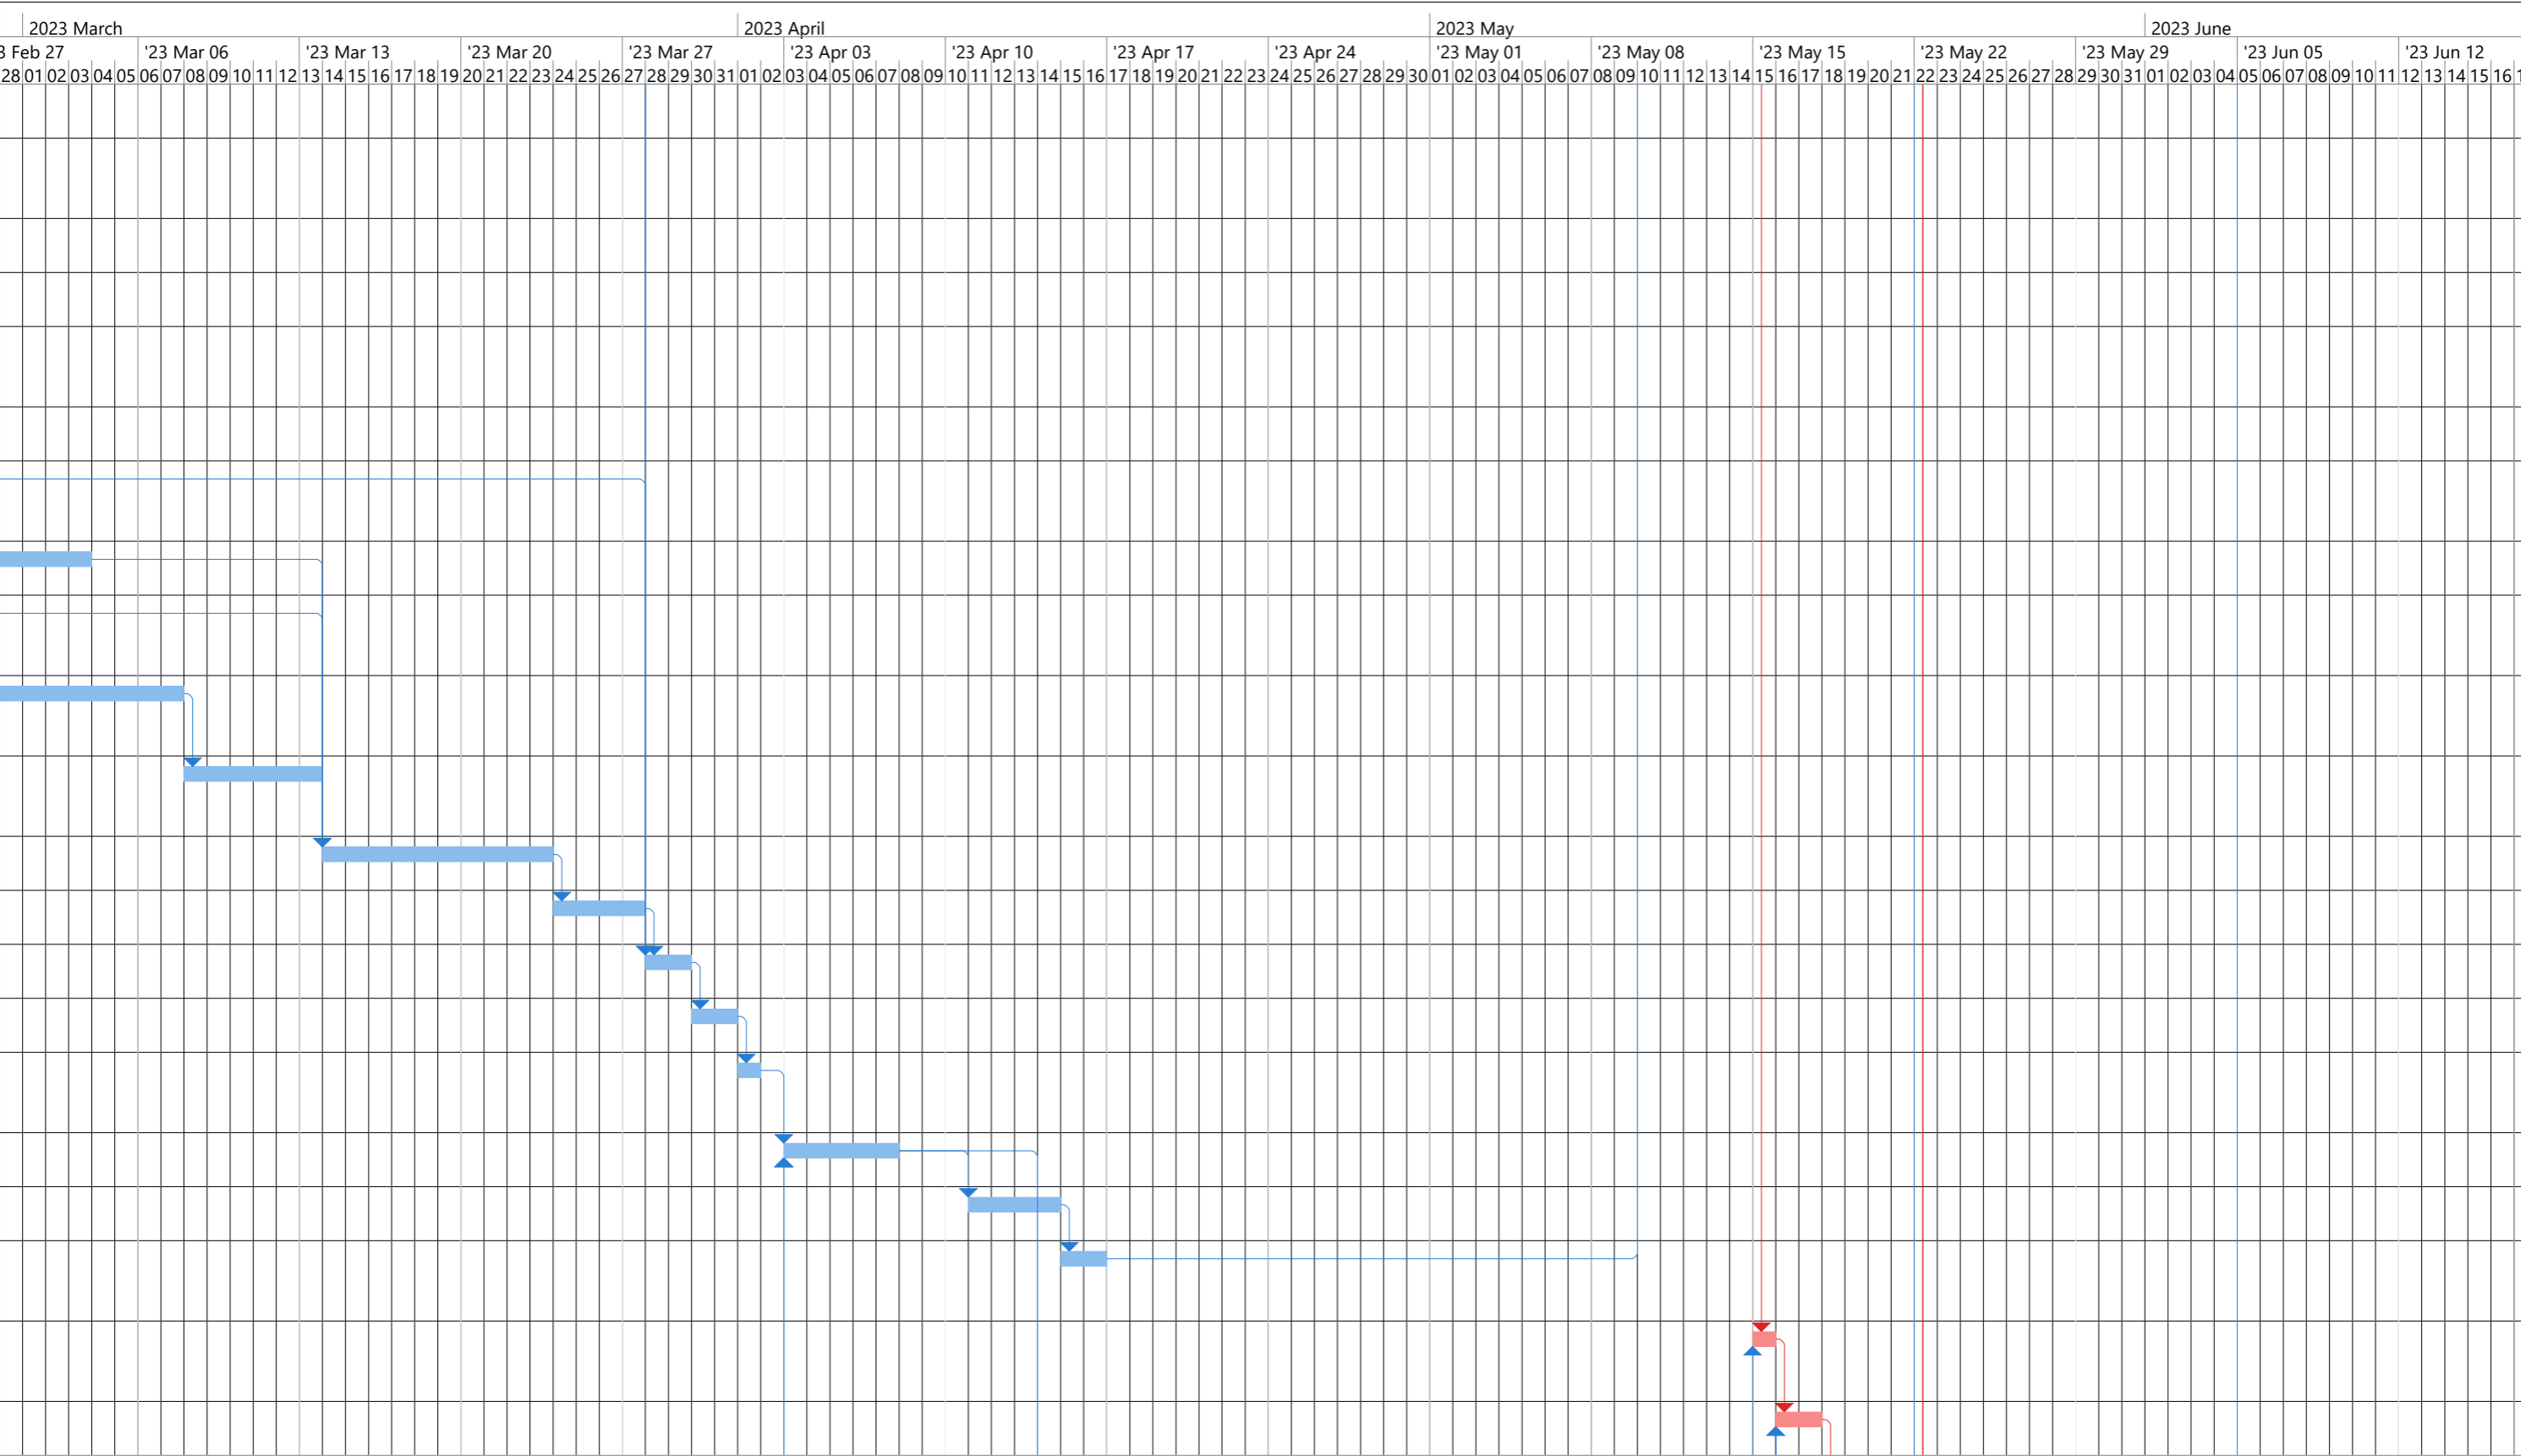

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task	<div></div>	Inactive Task	<div></div>	Manual Summary Rollup	<div></div>	External Milestone	<div></div>	Manual Progress	<div></div>
Split	<div></div>	Inactive Milestone	<div></div>	Manual Summary	<div></div>	Deadline	<div></div>		
Milestone	<div></div>	Inactive Summary	<div></div>	Start-only	<div></div>	Critical	<div></div>		
Summary	<div></div>	Manual Task	<div></div>	Finish-only	<div></div>	Critical Split	<div></div>		
Project Summary	<div></div>	Duration-only	<div></div>	External Tasks	<div></div>	Progress	<div></div>		

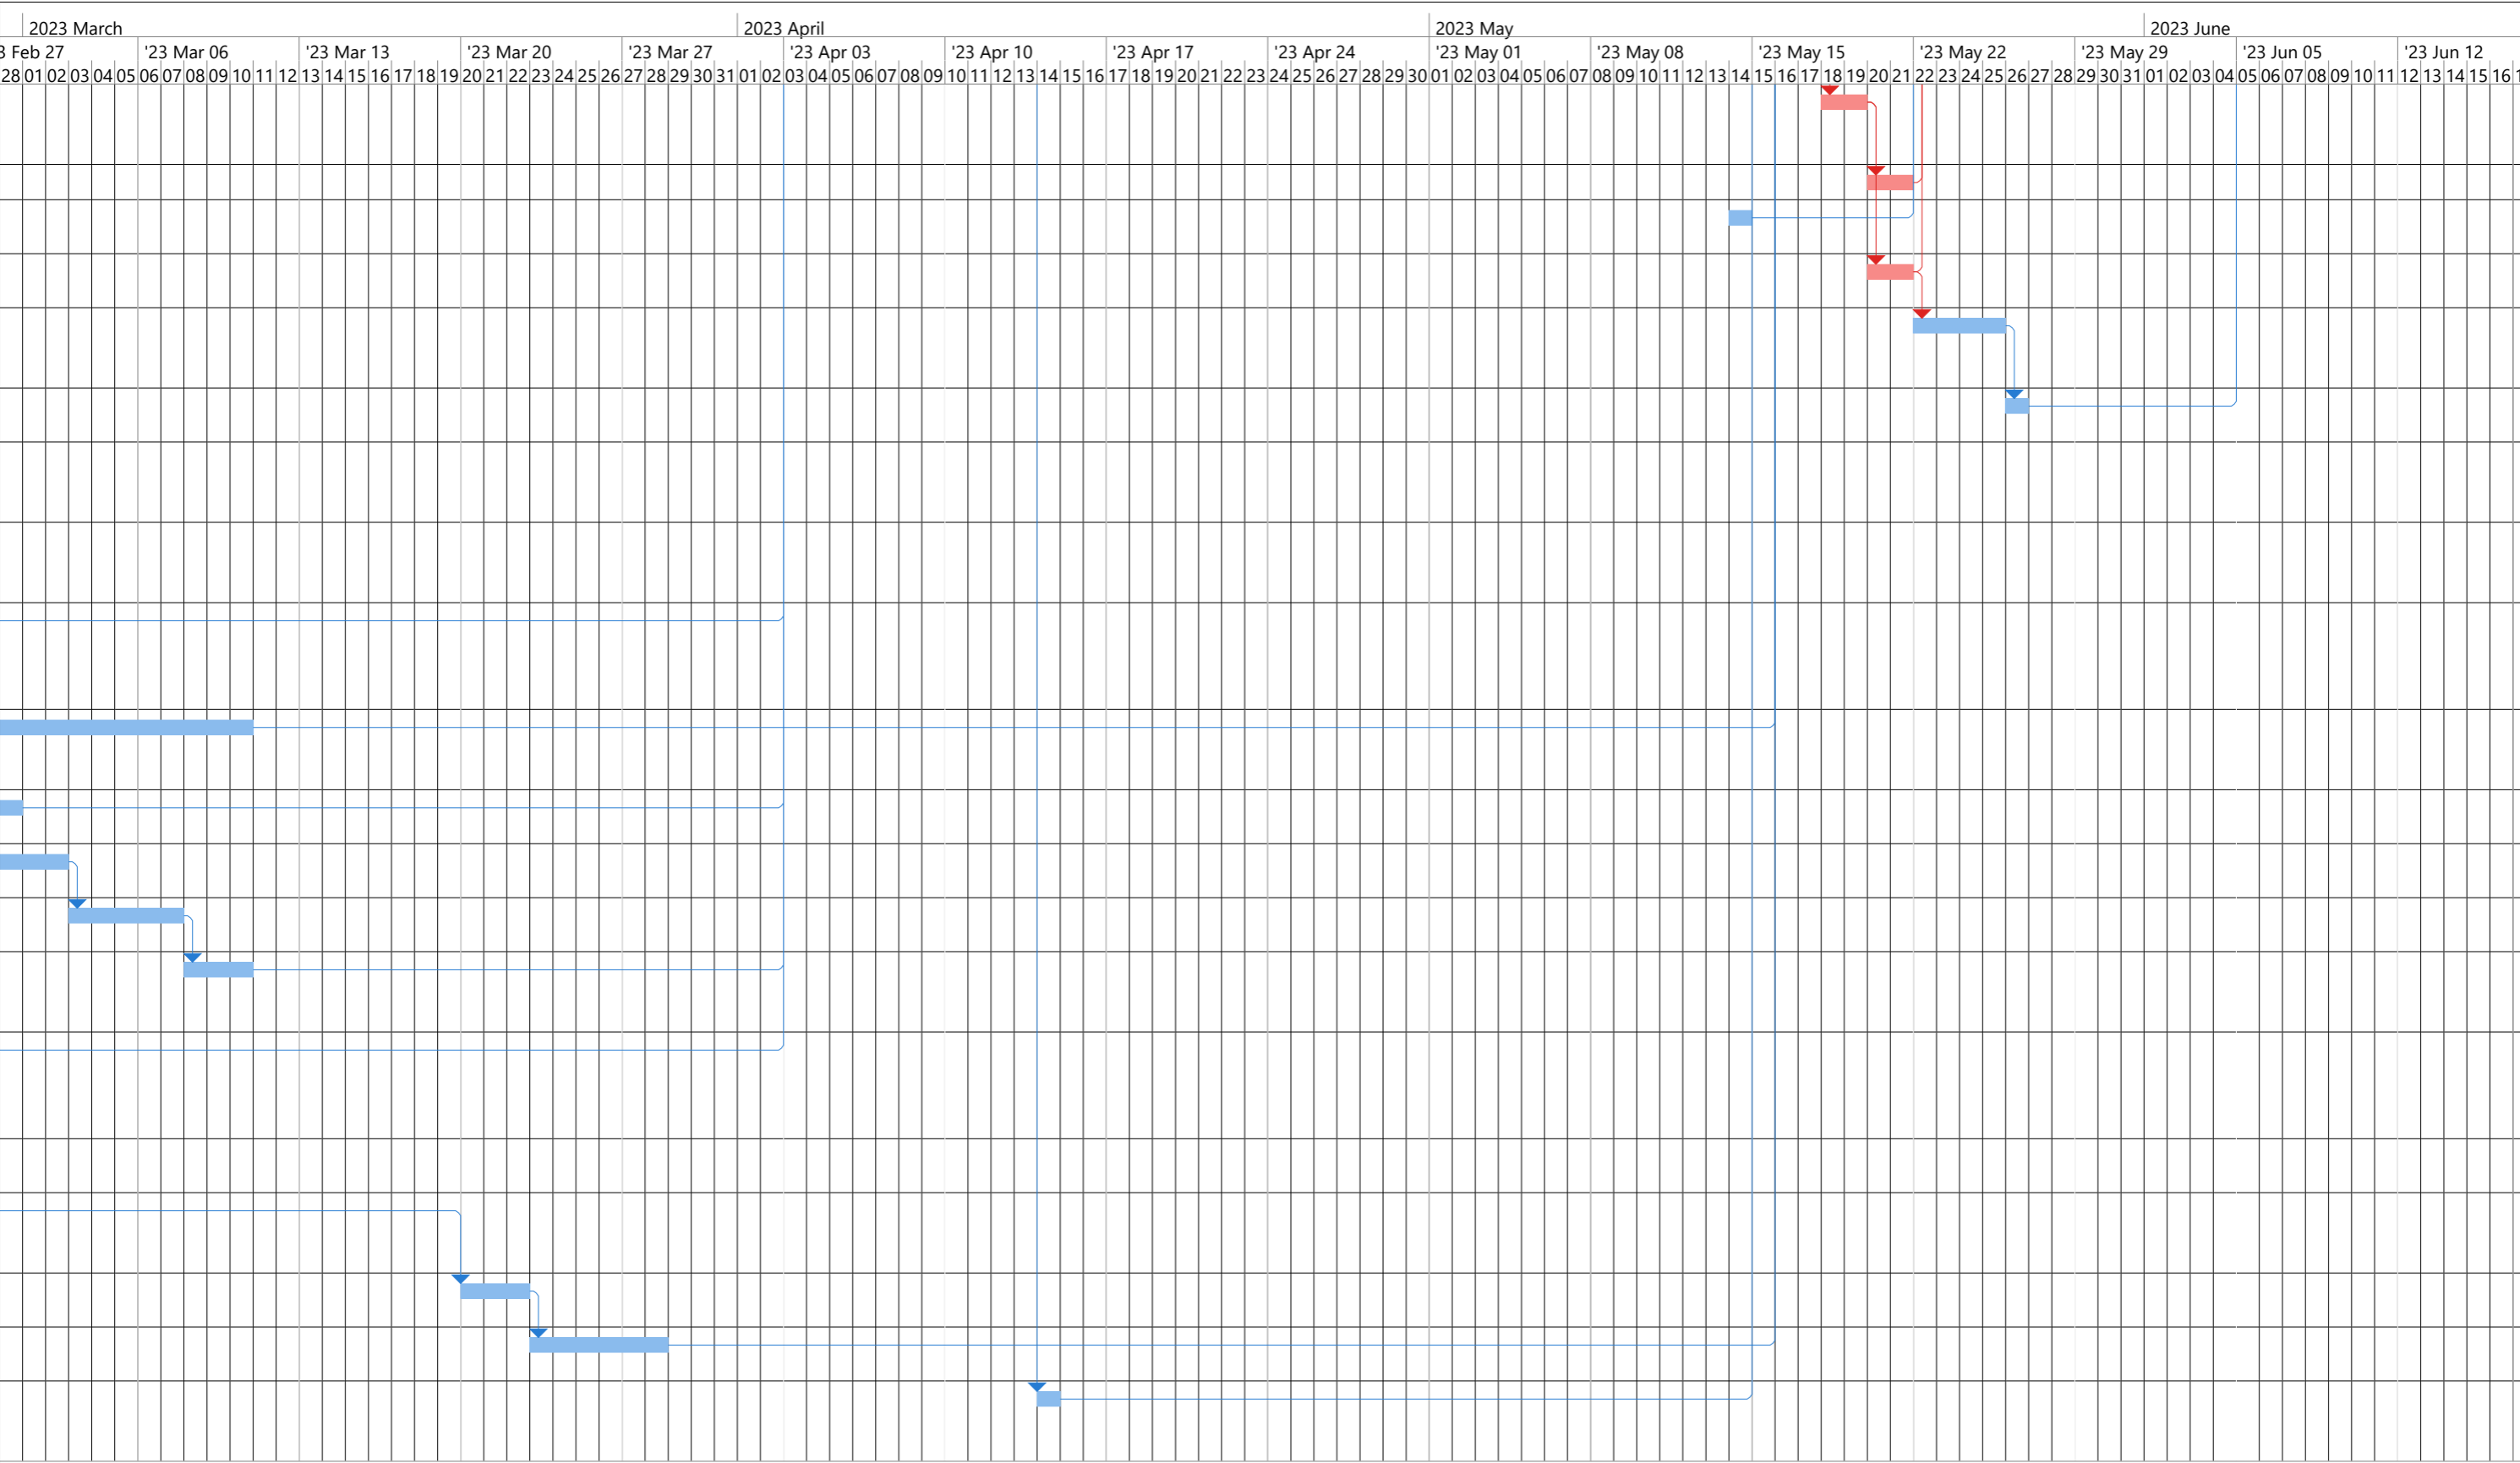

Project: T-8 remonto grafikas 2
Date: Tue 22-09-27

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress
